



Music City Star East Corridor Commuter Rail Monthly Construction Update – December 2005

Highlights / Accomplishments

- Construction of the By-Pass Track in Southern Junction was completed
- All Phases and CTC signal installation continues.
- The base stone and the curbs were installed at the Lebanon Station
- Grading work and platform work continued at the Donelson Station
- Grading work and platform work continued at the Hermitage Station
- Driveway, platform and utility work continued at Riverfront Station

Critical Issues

- Awarding Phase II work to the station and track contractors now that funds are available.


Construction Safety

- Roadway worker safety training continued to be given to the Contractor's Personnel along with Employee-In-Charge training.
- Weekly Construction meetings were held with all the Contractors.
- There were no lost time injuries on the site this month.

90 Day Look Ahead

- Queen City will conclude all work currently under contract.
- Stansell Electric will continue installing grade crossing signals on Phase II crossings and continue installation of train signals.
- Mt. Juliet and Lebanon Station paving and curb work will continue.
- Platform, grading and utility work will continue at Donelson and Hermitage.

Construction Pictures

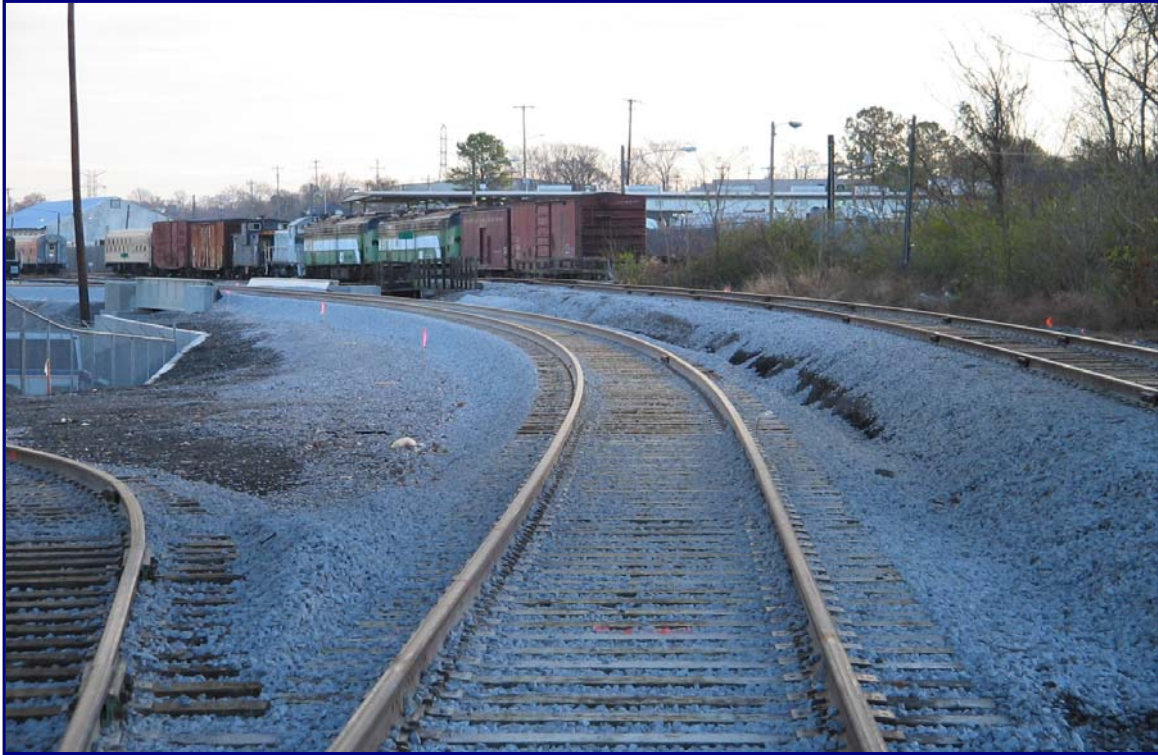

December 12, 2005 – Completed Southern Junction By-Pass Track



December 27, 2005 – Riverfront Station Building Framing
